


Delta Heritage Trail

12/12/24



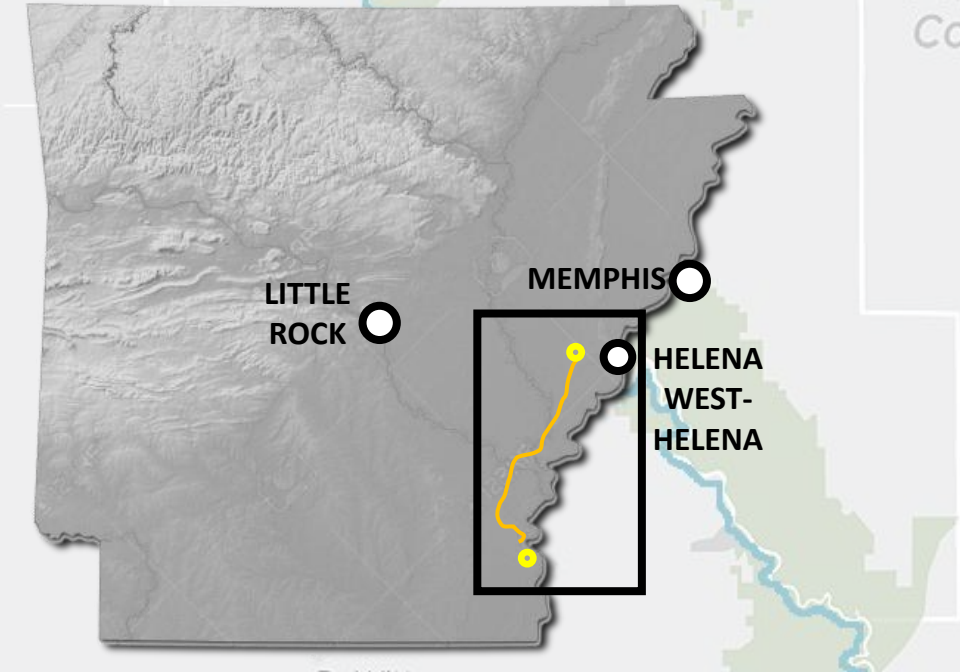


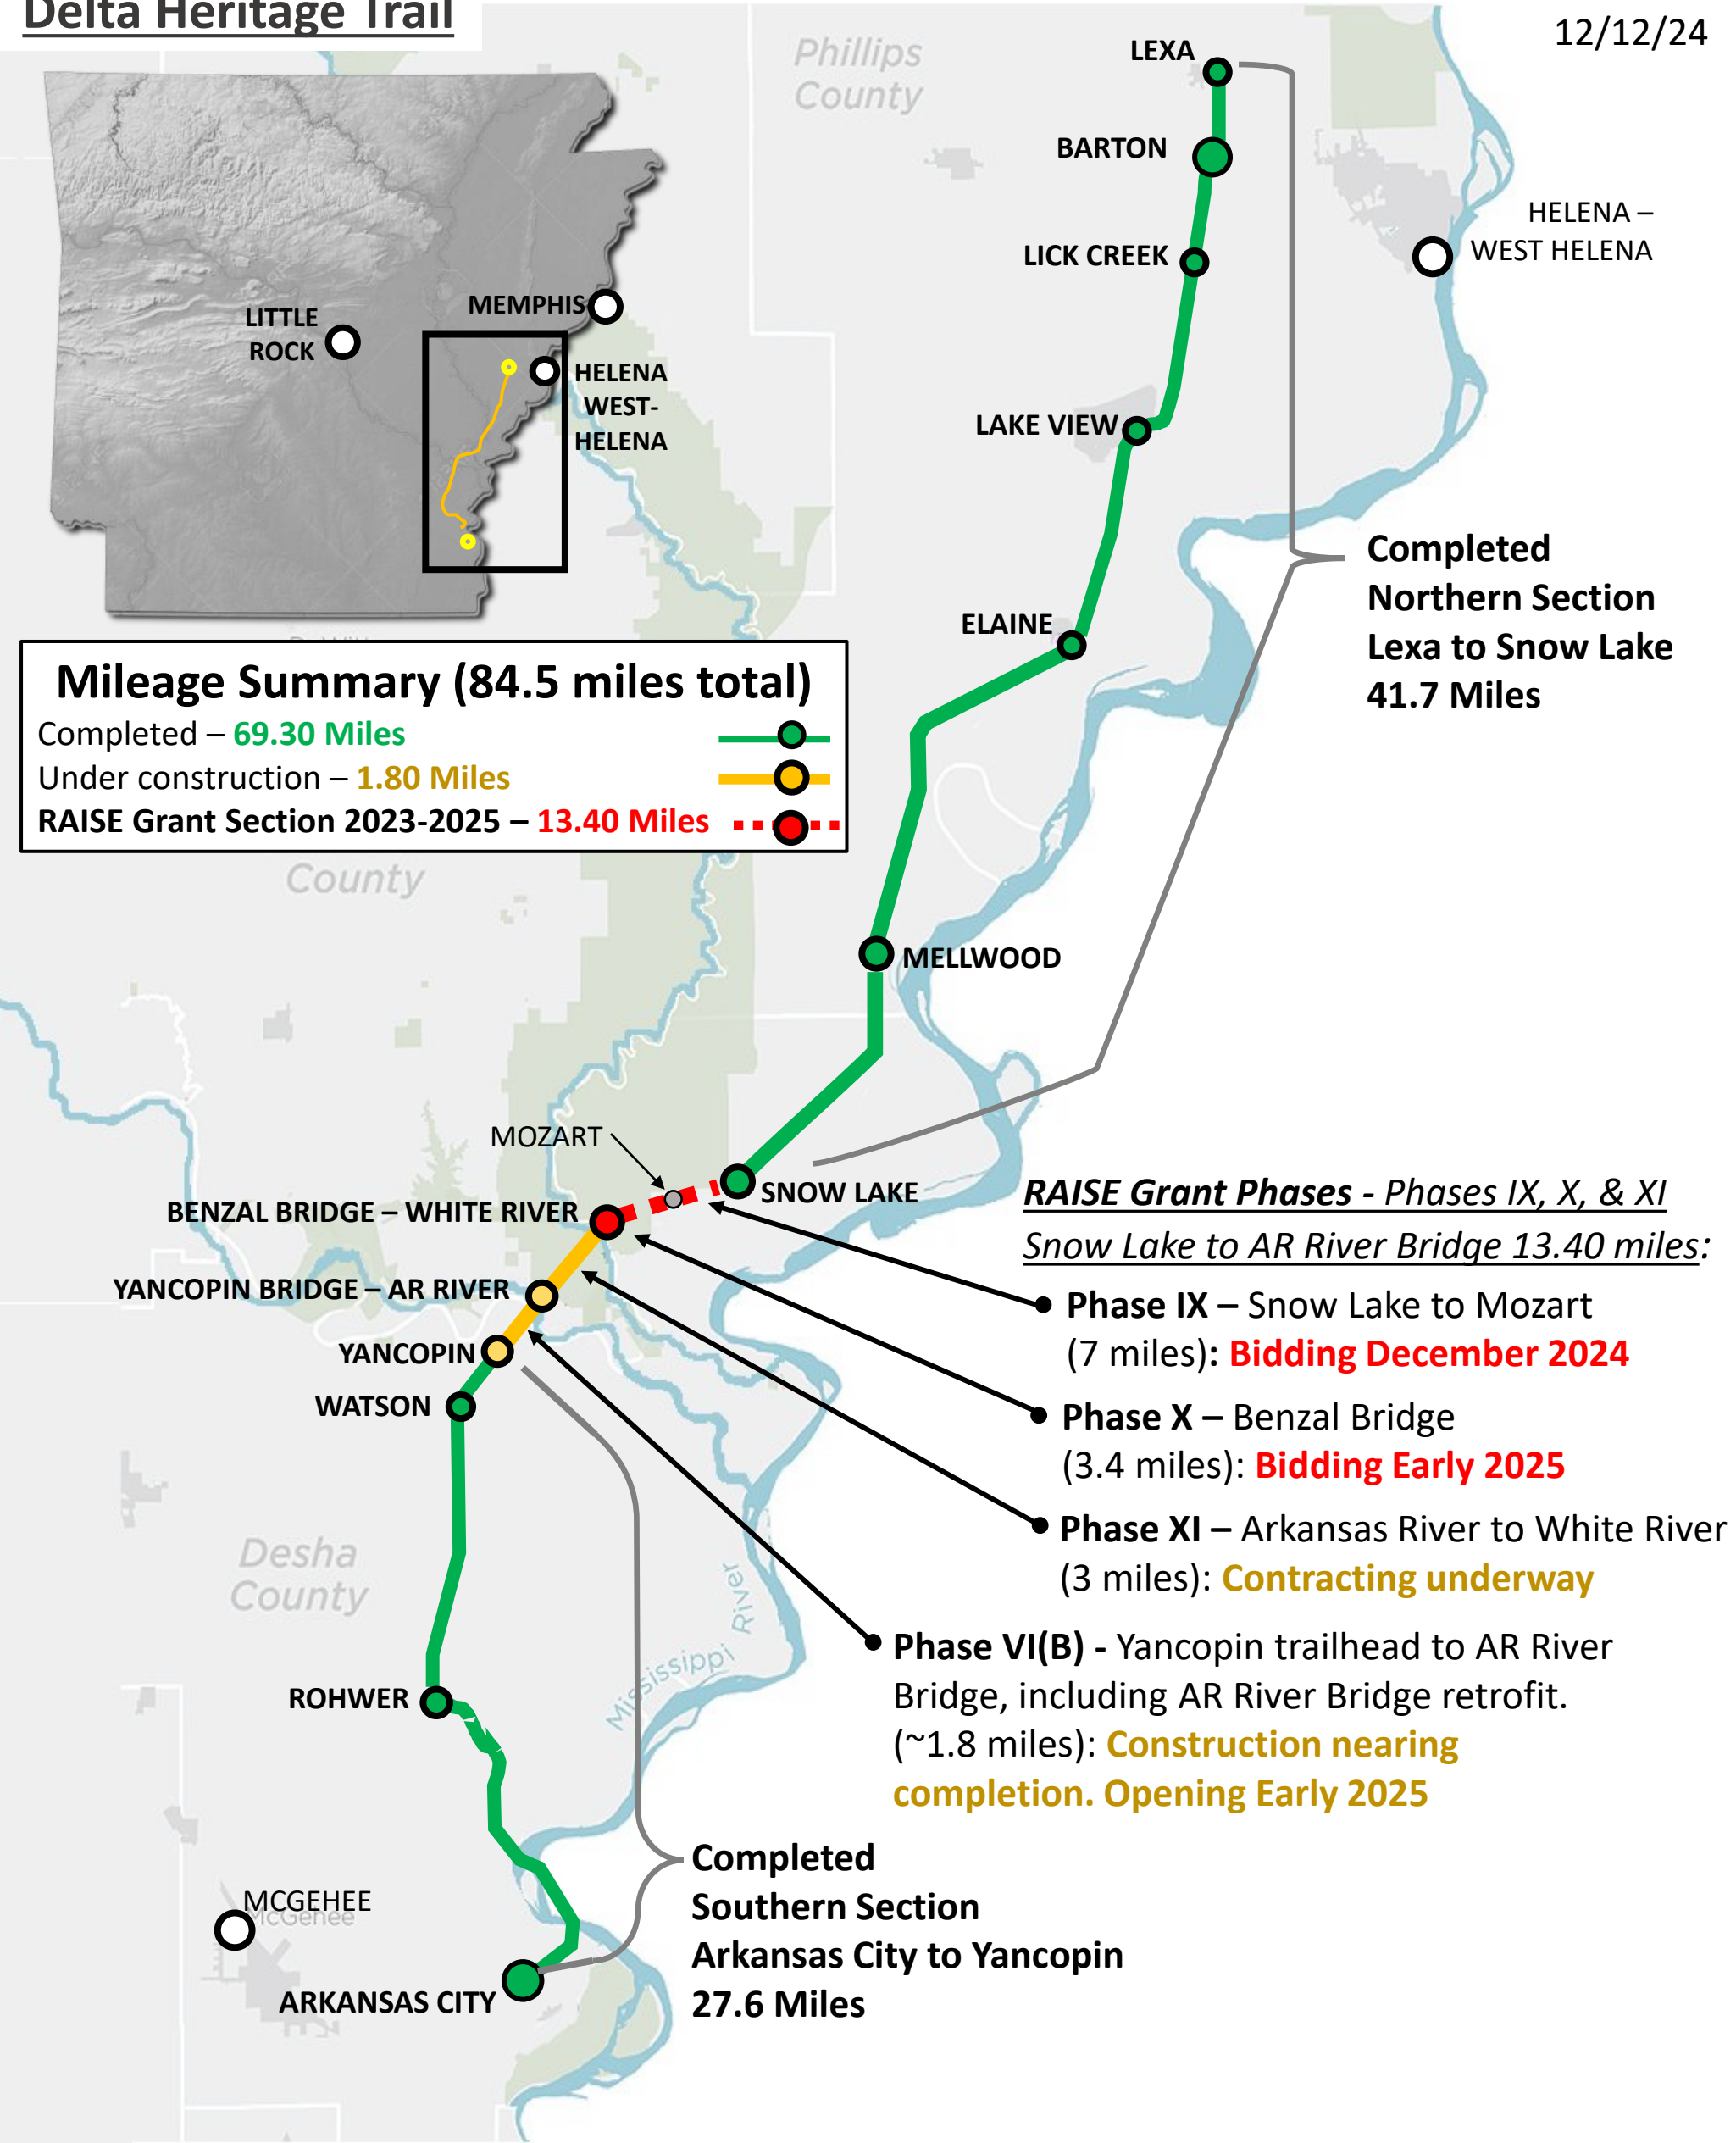
Mileage Summary (84.5 miles total)

Completed – 69.30 Miles

Under construction – 1.80 Miles

RAISE Grant Section 2023-2025 – 13.40 Miles





Completed
Northern Section
Lexa to Snow Lake
41.7 Miles

RAISE Grant Phases - Phases IX, X, & XI
Snow Lake to AR River Bridge 13.40 miles:

- **Phase IX** – Snow Lake to Mozart (7 miles): **Bidding December 2024**
- **Phase X** – Benzal Bridge (3.4 miles): **Bidding Early 2025**
- **Phase XI** – Arkansas River to White River (3 miles): **Contracting underway**
- **Phase VI(B)** - Yancopin trailhead to AR River Bridge, including AR River Bridge retrofit. (~1.8 miles): **Construction nearing completion. Opening Early 2025**

Completed
Southern Section
Arkansas City to Yancopin
27.6 Miles
